

Falmouth Route 1


Infrastructure Improvements

Pre-Construction

4.30.14

ID	Task Name	Duration	Start	Finish	May 4, '14	May 11, '14	May 18, '14	May 25, '14	Jun 1, '14	Jun 8, '14	Jun 15, '14	Jun 22, '14	Jun 29, '14	Jul 6, '14	Jul 13, '14	Jul 20, '14	Jul 27, '14	Aug 3, '14	Aug 10, '14	Aug 17, '14	Aug 24, '14	Aug 31, '14	Sep 7, '14	Sep 14, '14	Sep 21, '14	Sep 28, '14	Oct 5, '14	Oct 12, '14	Oct 19, '14
1	Mobilization	5 days	Mon 5/5/14	Fri 5/9/14																									
2	Survey / Signage	5 days	Mon 5/5/14	Fri 5/9/14																									
3	Phase 1	30 days	Mon 5/12/14	Fri 6/20/14																									
4	Test Pit Excavation	1 day	Mon 5/12/14	Mon 5/12/14																									
5	Tree Removal	4 days	Mon 5/12/14	Thu 5/15/14																									
6	STA 280+25W	2 days	Mon 5/12/14	Tue 5/13/14																									
7	Relocate Hydrant	1 day	Mon 5/12/14	Mon 5/12/14																									
8	DMH1A	1 day	Tue 5/13/14	Tue 5/13/14																									
9	Demo Headwall	1 day	Mon 5/12/14	Mon 5/12/14																									
10	Install 18" Storm Drain	1 day	Tue 5/13/14	Tue 5/13/14																									
11	Rip Rap	1 day	Tue 5/13/14	Tue 5/13/14																									
12	STA 282+50W	2 days	Wed 5/14/14	Thu 5/15/14																									
13	Convert CB10	1 day	Wed 5/14/14	Wed 5/14/14																									
14	Install 12" Storm Drain	1 day	Thu 5/15/14	Thu 5/15/14																									
15	CB B1	1 day	Thu 5/15/14	Thu 5/15/14																									
16	CB B2	1 day	Thu 5/15/14	Thu 5/15/14																									
17	CB B3	1 day	Thu 5/15/14	Thu 5/15/14																									
18	STA 286+45W	1 day	Fri 5/16/14	Fri 5/16/14																									
19	4" Sewer Service Replace	1 day	Fri 5/16/14	Fri 5/16/14																									
20	STA 287+55W	1 day	Fri 5/16/14	Fri 5/16/14																									
21	4" Sewer Service Replace	1 day	Fri 5/16/14	Fri 5/16/14																									
22	STA 276+00W - 293+00W	15 days	Mon 5/19/14	Fri 6/6/14																									
23	Electrical Duct Bank West Side	15 days	Mon 5/19/14	Fri 6/6/14																									
24	STA 288+80W	1 day	Mon 5/19/14	Mon 5/19/14																									
25	4" Sewer Service Replace	1 day	Mon 5/19/14	Mon 5/19/14																									
26	STA 288+95W	1 day	Mon 5/19/14	Mon 5/19/14																									
27	4" Sewer Service Replace	1 day	Mon 5/19/14	Mon 5/19/14																									
28	STA 290+10W	1 day	Tue 5/20/14	Tue 5/20/14																									
29	4" Sewer Service Replace	1 day	Tue 5/20/14	Tue 5/20/14																									
30	STA 292+25W	1 day	Tue 5/20/14	Tue 5/20/14																									
31	4" Sewer Service Replace	1 day	Tue 5/20/14	Tue 5/20/14																									
32	STA 295+00W	1 day	Wed 5/21/14	Wed 5/21/14																									
33	Relocate Hydrant	1 day	Wed 5/21/14	Wed 5/21/14																									
34	STA 295+60W	1 day	Thu 5/22/14	Thu 5/22/14																									
35	4" Sewer Service Replace	1 day	Thu 5/22/14	Thu 5/22/14																									
36	STA 296+00W	1 day	Thu 5/22/14	Thu 5/22/14																									
37	4" Sewer Service Replace	1 day	Thu 5/22/14	Thu 5/22/14																									
38	STA 297+25W	1 day	Fri 5/23/14	Fri 5/23/14																									
39	4" Sewer Service Replace	1 day	Fri 5/23/14	Fri 5/23/14																									
40	STA 298+75W	3 days	Mon 5/26/14	Wed 5/28/14																									
41	Install CB E1	1 day	Mon 5/26/14	Mon 5/26/14																									
42	24" Storm Drain	1 day	Mon 5/26/14	Mon 5/26/14																									
43	Install CB E2	1 day	Tue 5/27/14	Tue 5/27/14																									
44	Install CB E3	1 day	Tue 5/27/14	Tue 5/27/14																									
45	18" Storm Drain	1 day	Wed 5/28/14	Wed 5/28/14																									
46	STA 302+30W	1 day	Thu 5/29/14	Thu 5/29/14																									
47	4" Sewer Service Replace	1 day	Thu 5/29/14	Thu 5/29/14																									
48	STA 302+95W	1 day	Thu 5/29/14	Thu 5/29/14																									
49	4" Sewer Service Replace	1 day	Thu 5/29/14	Thu 5/29/14																									
50	STA 310+50W	1 day	Fri 5/30/14	Fri 5/30/14																									
51	Remove / Replace Hydrant	1 day	Fri 5/30/14	Fri 5/30/14																									
52	STA 315+00W	1 day	Mon 6/2/14	Mon 6/2/14																									
53	4" Sewer Service Replace	1 day	Mon 6/2/14	Mon 6/2/14																									

Falmouth Route 1
Infrastructure Improvements
Pre-Construction
4.30.14

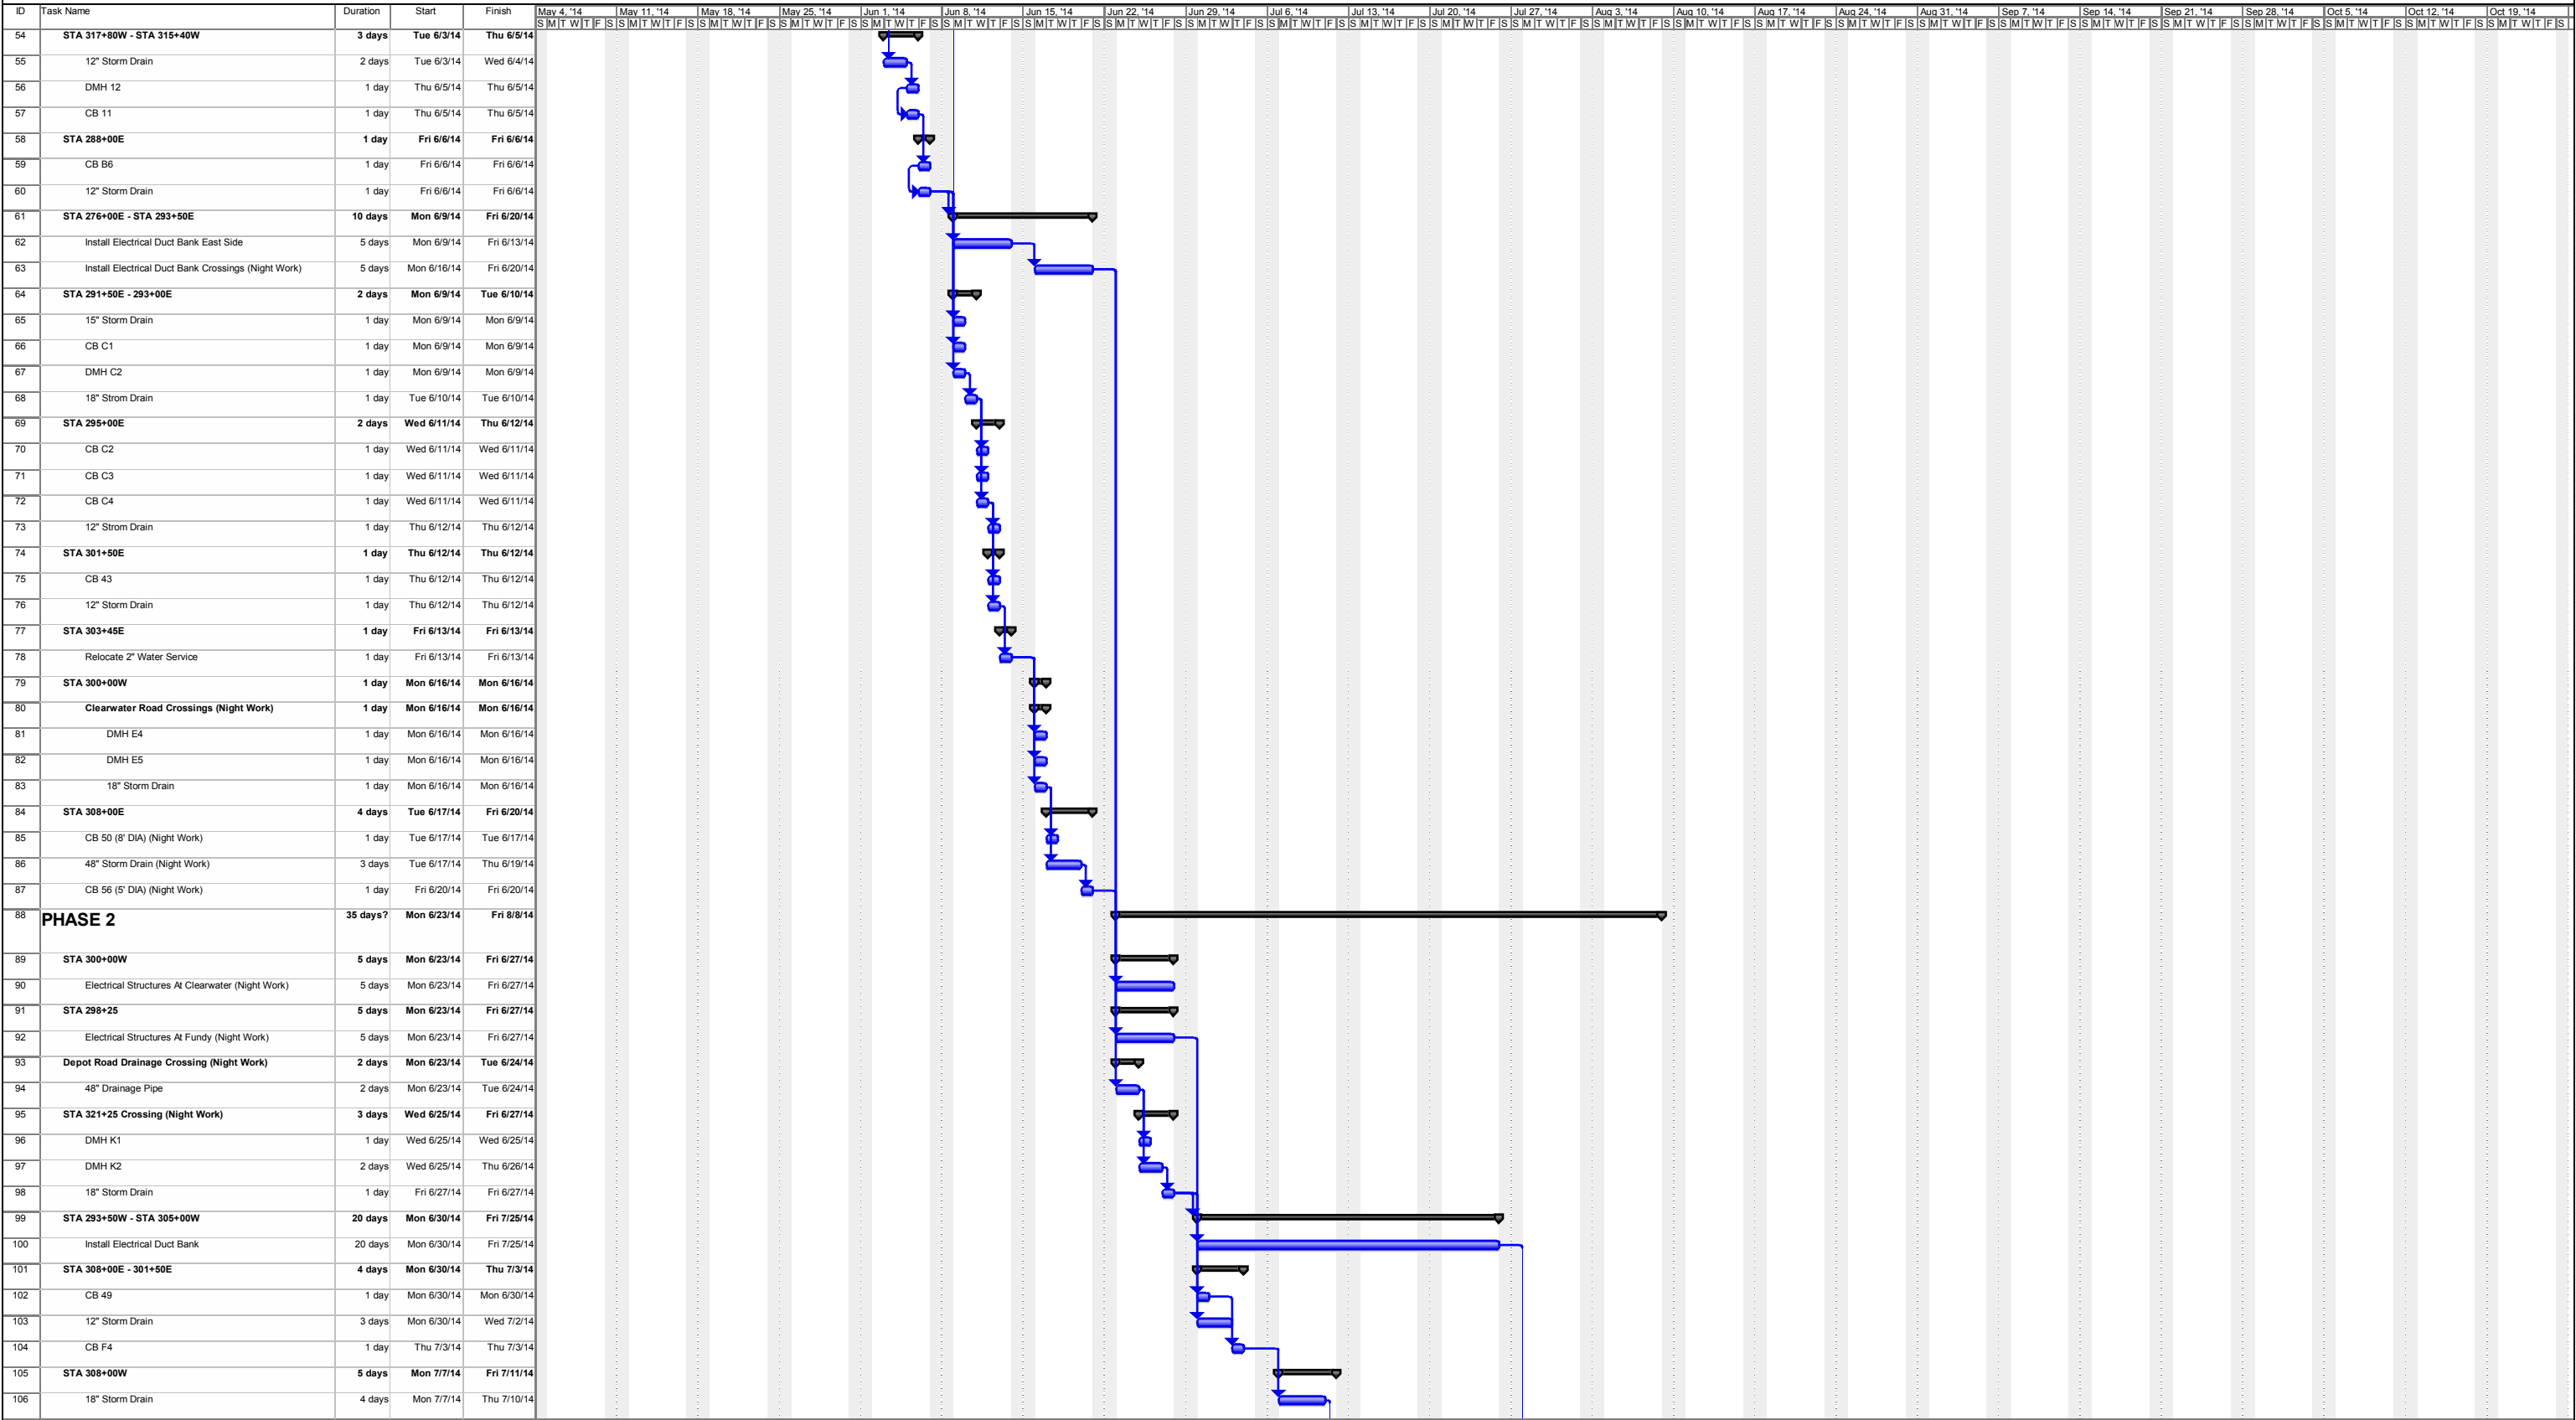

Falmouth Route 1

Infrastructure Improvements

Pre-Construction

4.30.14

